Iconic University

Sokoto Nigeria

Smart Government Service Delivery Platform

CivicFlow

Project Monitoring and Evaluation Records

Weekly reporting sprint controls and contribution evidence

Group 1

MIT 820 Software Development Project I

Group member	Registration number
Aminu Idris	2630802400002
Saidu Mustapha Suleman	2630802400001
Bolaji Watson	2630802400009
John Ojuekaiye Mayowa	2630802400008
Egbue Odira Celestine	2630803400003

Document version 1.1 Application baseline 1.0.4 23 October 2026

Final presentation 28 November 2026
Portal submission 29 November 2026 before 11:59 p.m. WAT

1 Recording and review procedure

This pack provides the records required to monitor Group 1 against MIT 820. Bolaji maintains the registers, while each member supplies evidence for their own work. Enter actual meeting dates, decisions, completed work and review results. The prepared fields and proposed backlog are planning records until completed and reviewed.

The repository contains editable Markdown templates and CSV registers alongside this printable pack. Link actual GitHub issues, commits and pull requests after the repository is uploaded. Each weekly report includes work completed, work planned, blockers and the current live-build link.

2 Weekly progress report form

Reporting period _____ Report number _____

Prepared by _____ Date _____

Current live build URL and release _____

Independent access check and date _____

Work completed and evidence

_____

_____

Work planned for the next period

_____

_____

Blockers and support required

_____

_____

Risks or scope changes

_____

_____

Supervisor feedback and next review

_____

_____

3 Supervisor meeting minutes form

Meeting date and time WAT _____

Meeting mode or location _____

Attendees and apologies _____

Agenda and relevant requirement or gate _____

Decision and approval conditions _____

Next review date _____

Action	Owner	Due date	Evidence and status
_____	_____	_____	_____
_____	_____	_____	_____
_____	_____	_____	_____

4 Sprint plan and review

Sprint	Dates in 2026	Review focus
1	23 October to 1 November	Scope, SRS, architecture, models and repository baseline.
2	2 to 15 November	Integration, security boundaries, usability and defect correction.
3	16 to 27 November	Hosted acceptance, recovery, final documents and rehearsal.

The proposed backlog totals 79 points. An estimate is a planning unit rather than a duration or assessment mark. At sprint planning the group confirms scope and capacity. A done item must have linked evidence and review. Preserve the original estimate and record scope changes separately so the remaining-work history is intelligible.

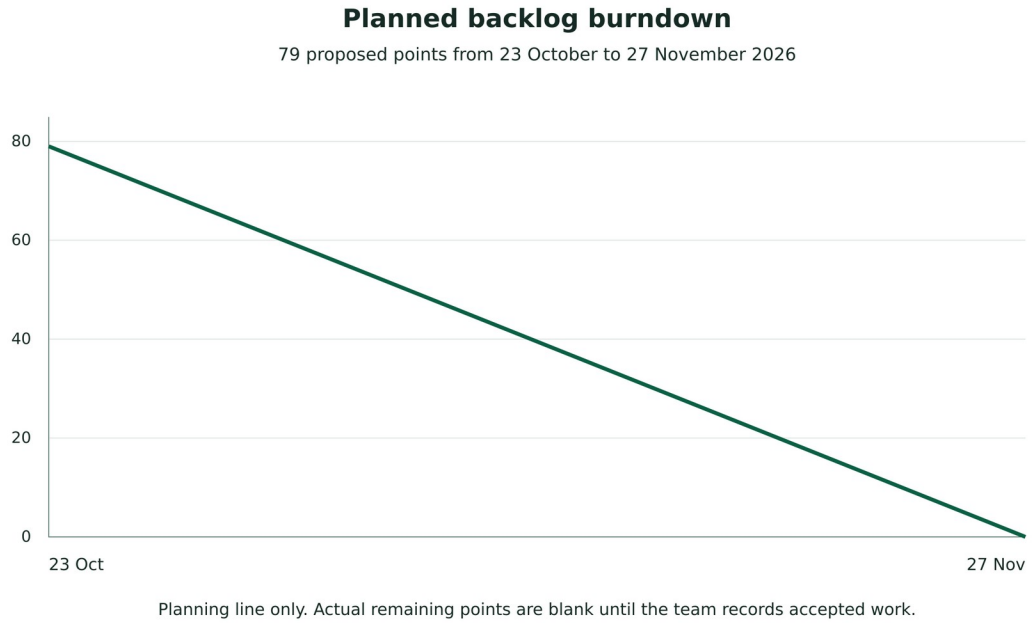


Figure 4.1 Planned backlog burndown

Sprint review date and attendees _____

Accepted items and evidence _____

Unfinished items and reason _____

Retrospective action owner and due date _____

5 Risk and issue register

ID and risk	Owner	Treatment	Review evidence
R01 Approval evidence missing	Bolaji	Obtain dated proposal record and conditions.	_____
R02 Hosted system inaccessible	Aminu	Independent access check and local contingency.	_____
R03 Private records exposed	Aminu	Repeat permission, upload and protected-path tests.	_____
R04 Scope or provider delay	Bolaji	Prioritise core workflow and record provider dependencies.	_____
R05 Insufficient quality evidence	John	Complete browser, capacity and recovery records.	_____
R06 Contribution history incomplete	All members	Link actual commits, reviews and peer assessment.	_____

6 Individual contribution and peer assessment

Member and registration	Allocated responsibility	Evidence and reviewer
Aminu Idris 2630802400002	Development	Commit or PR _____ Artifact _____ Reviewer _____
Saidu Mustapha Suleman 2630802400001	Documentation	Commit or PR _____ Artifact _____ Reviewer _____
Bolaji Watson 2630802400009	Project management	Commit or PR _____ Artifact _____ Reviewer _____
John Ojuekaiye Mayowa 2630802400008	Development	Commit or PR _____ Artifact _____ Reviewer _____
Egbue Odira Celestine 2630803400003	Documentation	Commit or PR _____ Artifact _____ Reviewer _____

Each member records the problem addressed, files or artifacts changed, test or review evidence and the corresponding issue or pull request. Peer assessment should describe the actual contribution and collaboration observed. Do not reconstruct Git commits or backdate records to imply work that the repository history does not contain.

7 Consent and usability observation

Explain the purpose, tasks, voluntary participation, information recorded, storage period and contact person before a usability session. Use an approved consent process. Permit withdrawal, avoid recording passwords or private cases, and use an anonymised participant ID. Obtain separate permission for any audio or screen recording and follow the university supervisor’s requirements.

Field	Observation
Participant ID and consent reference	_____
Task and environment	_____
Completion and assistance required	_____
Error, time and participant comment	_____
Action, owner and review date	_____

8 Hosted test and recovery record

Environment URL and application release _____

Database and PHP version _____

Test date checker and evidence _____

Workload method and response-time result _____

Backup reference and restore environment _____

Measured recovery point and recovery time _____

Failures defects and release decision _____

9 Final defence and submission record

Confirm the approved proposal, reviewed SRS and ADD, current report, manuals, tests, code and independent live access before defence. Keep the evaluation password in the agreed private channel. Rehearse the workflow and questions with all five members. After the 28 November presentation, record the panel's corrections and complete the portal submission before 11:59 p.m. WAT on 29 November.

Defence build and independent checker _____

Panel feedback and correction owner _____

Submission file list and final review _____

Portal submission date time and receipt reference _____

Project manager sign off _____
